TOM HUBBARD

128 Central Park Lane Evans, GA 30809 440-409-8003 info@tomhub.com www.tomhub.com


20 February 2017

Isabela Gould Neighborhood Design Center 1445 Summit Street, Suite 300 Columbus, OH 43201

RE: Streetcar Sculpture #2 on Livingston Avenue
McKay Lodge Conservation Laboratory Peer Review Report

- 1. Powder Coat with gloss clear coat
 - a. Aluminum plate profile: orbital sanded with 60 grit sandpaper Powder coat film build: Base coat 2.5 - 3.5mil Clear coat: 1.5mil
 - b. Powder Coat Brand: Prismatic Powders
 Chantilly Lace PWB-1795, Pacific Sunset PMB-5856, RAL-1033, RAL-3004,
 Clear Vision PPS-2974 (UV stable)
 - c. Powder coat applied by a custom shop using 3 stage iron phosphate process to promote bonding.
 - d. Maintenance/repair: Aerosol and liquid touch-up paint from Custom Color & Filling for repair in the field.
- 2. Separation of stainless steel and aluminum
 - a. Galvanic Corrosion: A nylon (approx. 0.02") gasket will be fabricated and placed between all stainless steel and aluminum connections.
 - b. Loctite will be used on all mechanical connections.


Tom Hubbard



PRODUCTION SCHEDULE

LIVINGSTON PARK STREETCAR SCULPTURE

1/11	Building Permit Issued	
1/23 – 2/17	New Site Plan to City	(4 weeks)
1-30 – 6/2	Fabrication	(18 weeks)
5/1 – 5/19	Foundations	(3 weeks)
5/15 -6/2	Inspection: Foundations	(3 weeks)
6/1 – 6/16	Installation	(2 weeks)
6/4 – 7/7	Inspection: Structure	(3 weeks)
6/14 - 6/30	Landscaping	(2 weeks)
7/17 –8/1	Dedication	

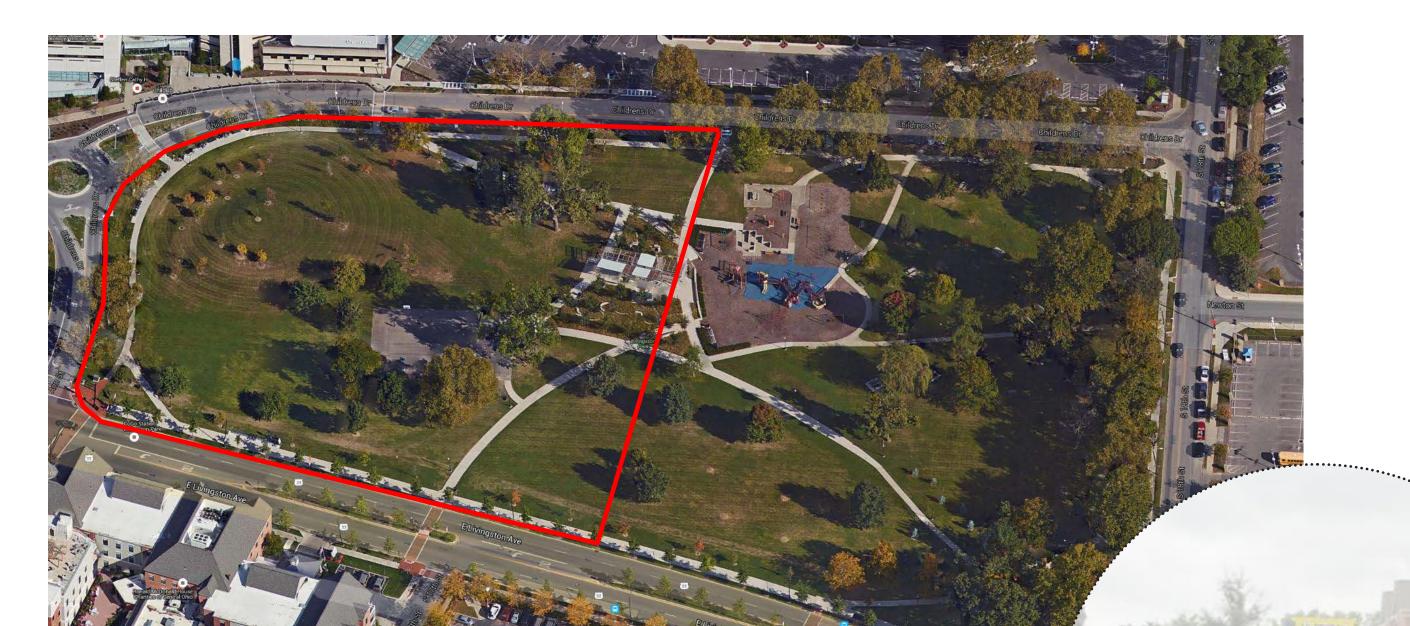


Depiction of Easement Area

Livingston Park Sculpture #2 Update

CAC meeting 02/28/2017




Original Site Plan

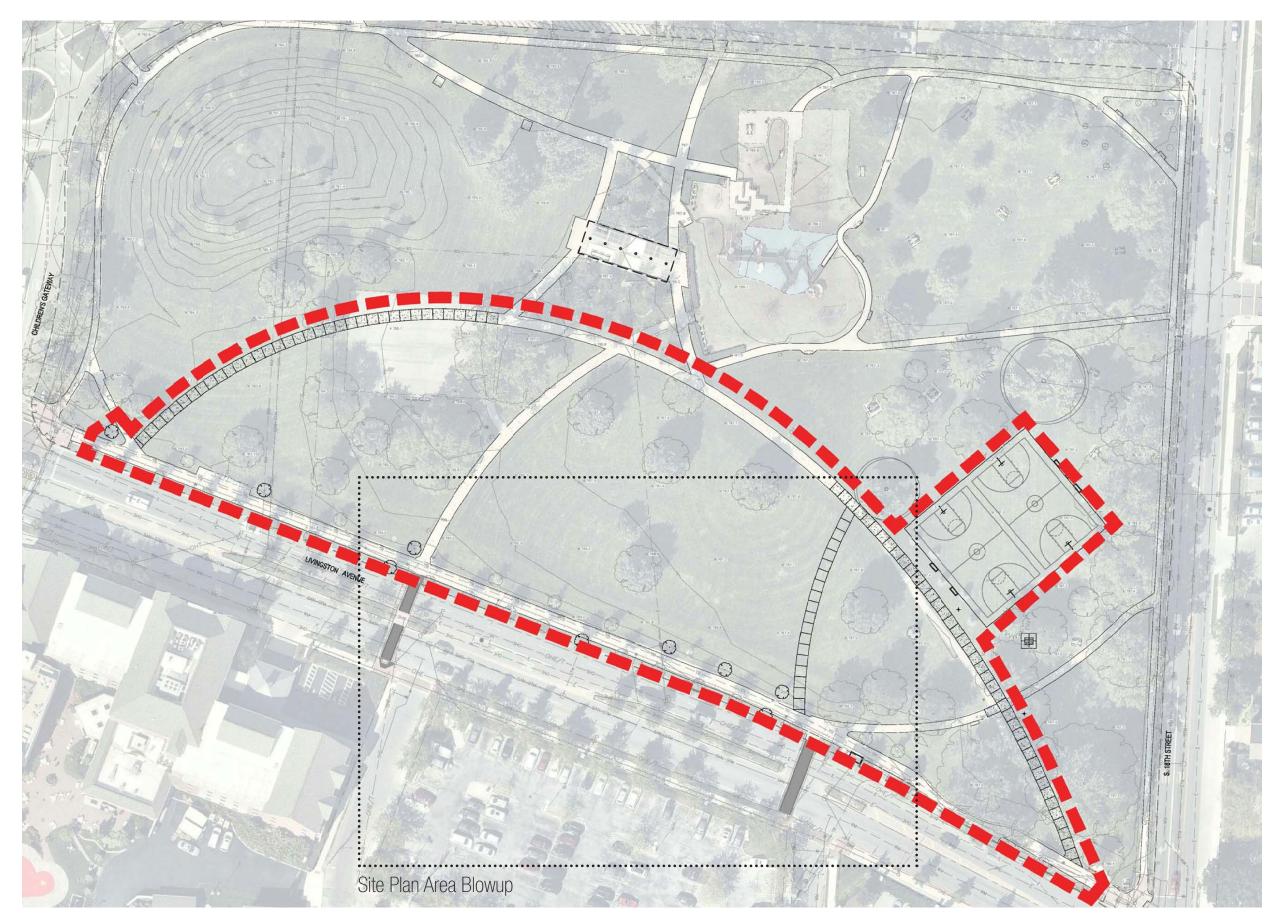





View from Livingston Ave sidewalk looking north where proposed path is to be located with sculpture Location C demarcated

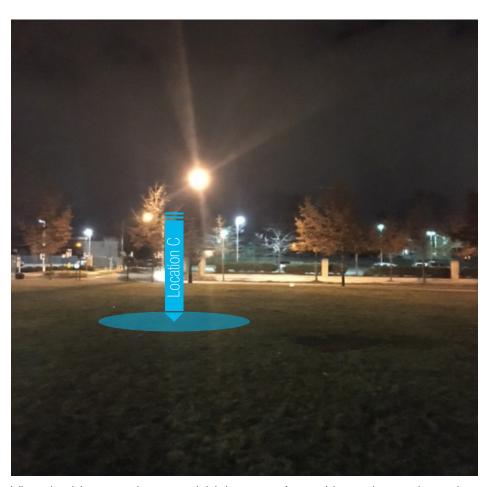

View looking south toward Livingston Ave with sculpture Location C demarcated



View from proposed path looking southwest with sculpture Location C demarcated



